Actions to stop doing:

- The team should stop making major code changes without first informing the group, as this has caused temporary bugs and merge conflicts.
- The team should stop postponing backend related tasks until later in the sprint, since this creates time pressure.

Actions to start doing:

- Start testing features on multiple platforms (ios and android) earlier in the sprint.
- Begin reviewing Firebase rules and database structure earlier when new features depend on backend data.
- Begin using a development branch so it does not interfere with the main branch/

Actions to keep doing:

- We should keep dividing user stories among members based on strengths and availability
- Continue using GitHub regularly to track progress and share updates
- Keep reviewing each other's work as things get pushed in order to ensure everything works.

Work completed/not completed:

- ☑ User Story 2.1
- ☑ User story 2.2
- ☑ User Story 2.3
- ☑ User Story 2.4
- ☑ User story 2.5

Work completion rate: 5/5

During Sprint 2, the team successfully completed most of the planned user stories. We ran into some IOS and Android compatibility problems with the pins showing up, so we allocated a lot of our time on bug fixing. Most user stories were completed on time, and team members generally contributed about 1 to 2 hours per day, with more time allocated during testing. As our familiarity with React Native, Firebase, and Expo improved, the development team's speed also increased compared to sprint one.

Burnup/Burndown chart:

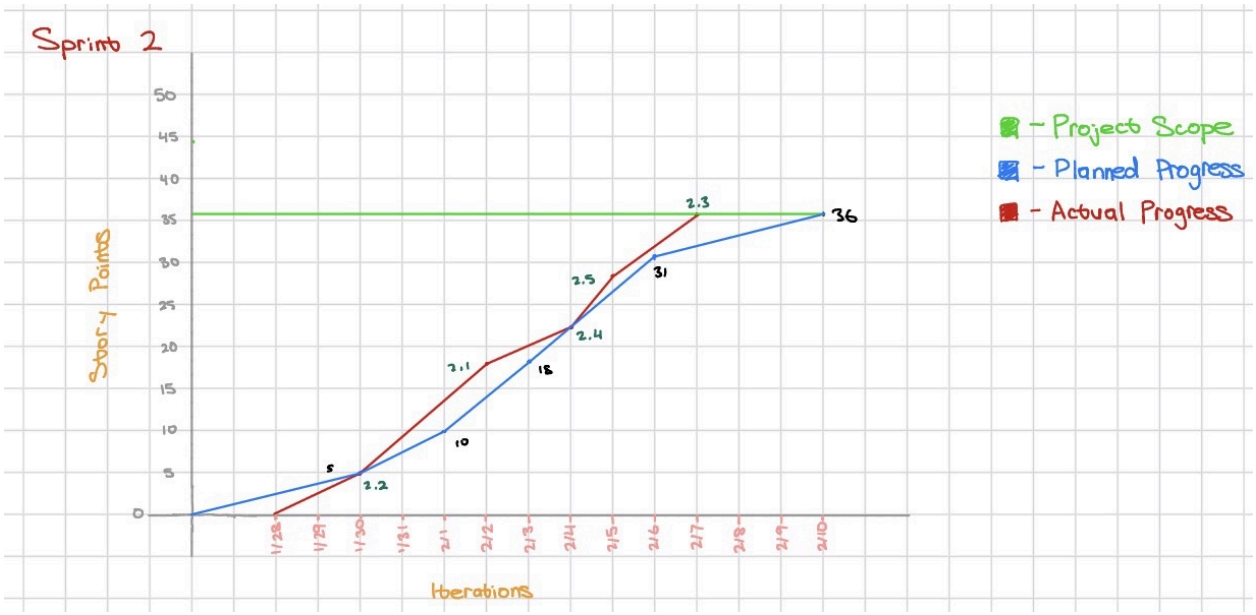
Sprint 2
Story Points
50
45
40
35
30
25
20
15
10
5
0
1/28
1/29
1/30
1/31
2/1
2/2
2/3
2/4
2/5
2/6
2/7
2/8
2/9
2/10
Iterations
5
2.2
10
2.1
18
2.4
31
2.5
2.3
36
- Project Scope
- Planned Progress
- Actual Progress
